

DEMOLITION NOTES

- 1 REMOVE AND RETURN TO OWNER.
- 2 LIGHTS ON LOOP CIRCUIT TO BE TESTED, REPAIR OR REPLACE AS NECESSARY FOR CONT'D. SERVICE. BY OWNER.
- 3 REMOVE CONCRETE WHEEL STOPS AND RETURN TO OWNER.
- 4 TO BE RELOCATED BY OTHERS PRIOR TO DEMOLITION.
- 5 NOT USED.
- 6 EXISTING TREES PROTECTED AND AVAILABLE FOR WATERING DURING CONST.
- 7 REMOVE STIMULANT WHERE SHOWN FOR REMOVAL. GENERAL CONTRACTOR MAY AT HIS OPTION, LEAVE EXISTING CURBS IF PROTECTED, OR REPLACE.
- 8 INITIALLY REMOVE ONLY + 10 FEET OF SLAB AT WEST SIDE, TO FACILITATE CONST. REMOVE REMAINING SLAB SHOWN. REMOVE TOE + ONE FOOT OF WALL, SAW CUT AT ENDS. REMOVE EARTH FILL PER STRUCT. DRWS.
- 9 REMOVE REMAINING WALL AND EARTH FILL COMPLETE. AT NUCLEAR, CUT WALL FLUSH WITH EXISTING WALL TO REMAIN. REMOVE EARTH FILL TO ONE FOOT BELOW NEW FINISH GRADE.

LEGEND

EXISTING BUILDING TO BE DEMOLISHED


EXISTING SITE CURBS & VEGETATION TO REMOVE

EXTENT OF BUILDING EXCAVATION

SITE PLAN - DEMOLITION

1" = 20' - 0"

NORTH

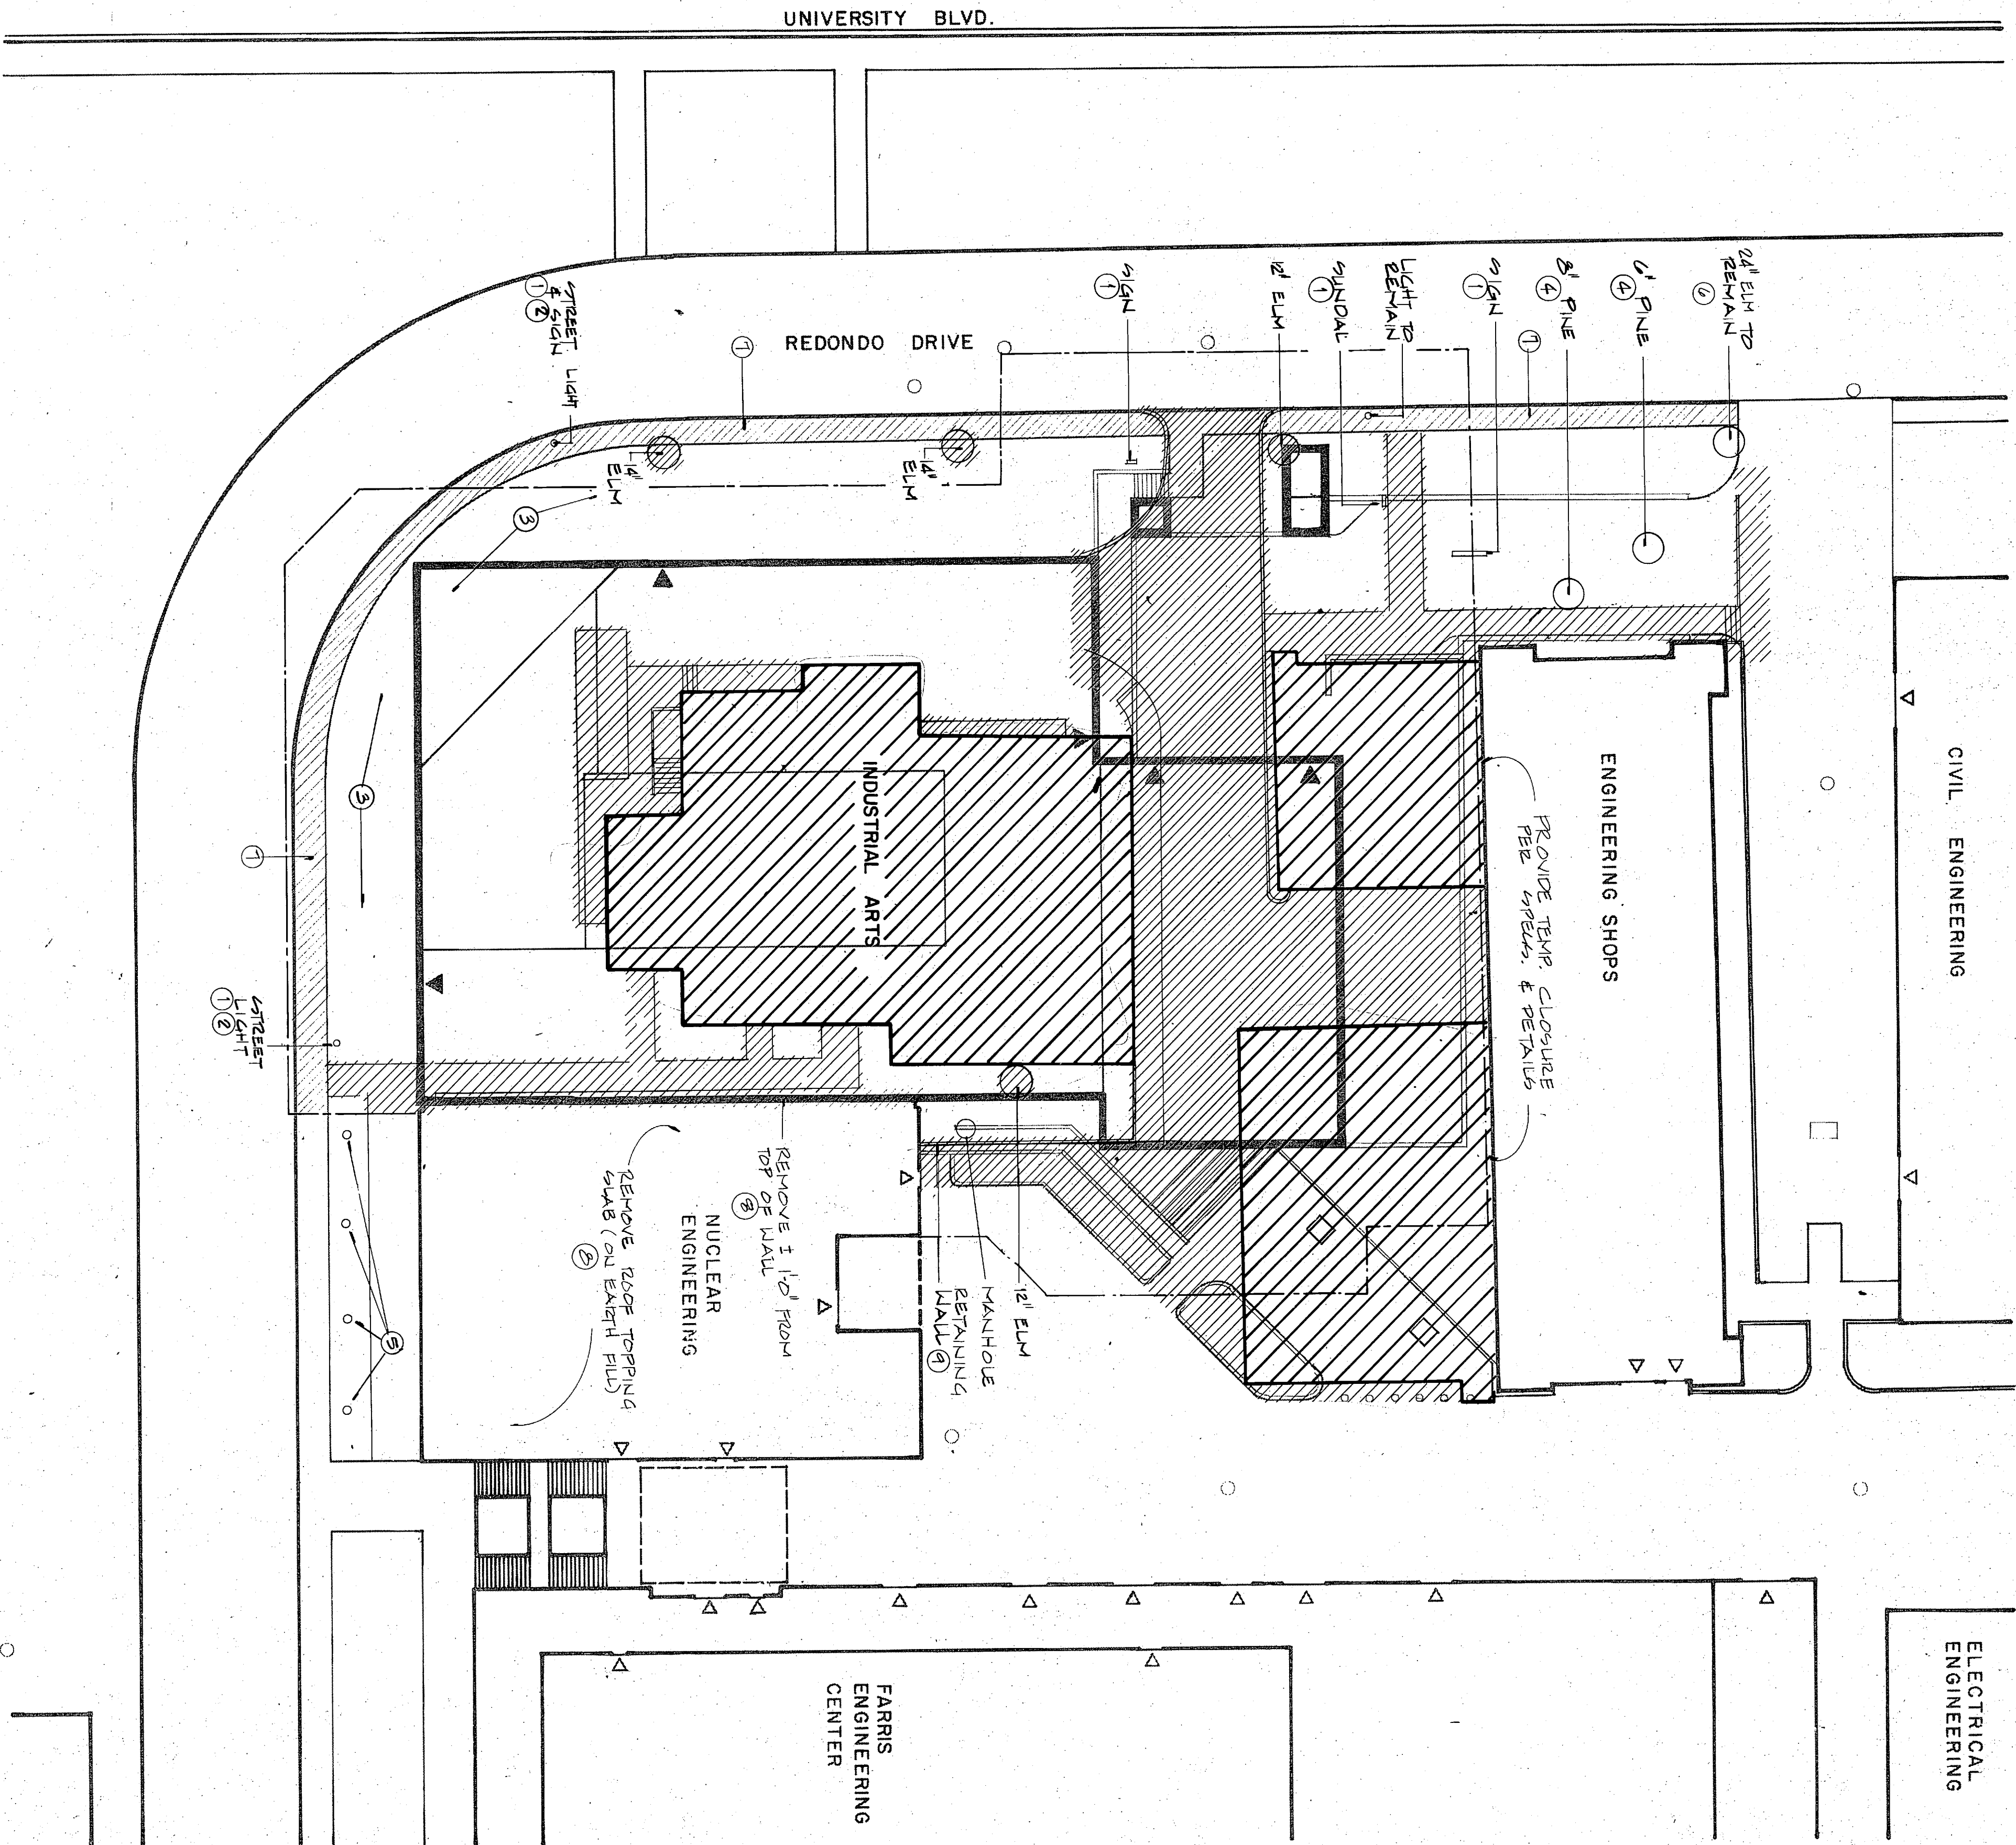

UNM MECHANICAL ENGINEERING BLDG

DEMOLITION PLAN - BASE BID

